

Building Exterior

- Window installation has begun
- Metal panel installation will begin later this month
- Exterior masonry work will be completed
- Roofing installation will be completed




Building Interior

- Wall framing work will begin in single story portion of the building
- The final slab on grade concrete floor pours will be completed
- CMU walls will continue



Building Interior MEP

- The electrical switchgear will be installed this month
- Plumbing and mechanical piping systems are being installed throughout
- HVAC ductwork is being installed on 1st & 2nd floors of classroom wing

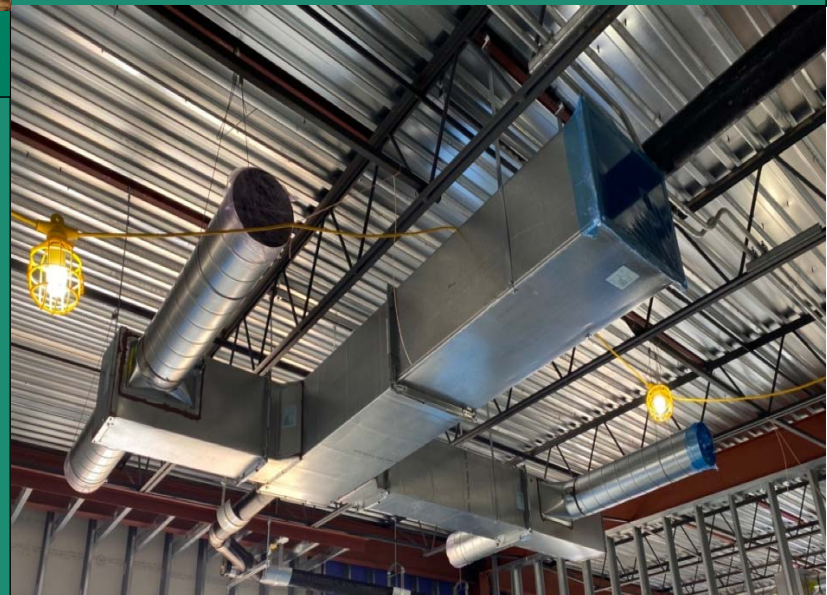



**ARROWHEAD ELEMENTARY SCHOOL PROJECT
NOVEMBER 2021 BOARD REPORT**



Upcoming Work – November – December 2021

- Complete TPO roof installation
- Complete pouring concrete floor slabs & steel stair pans
- Complete exterior masonry work including brick veneer
- Complete building envelope and begin providing temporary heating of building
- Continue with above-ceiling and inwall rough-ins of all MEP systems
- Continue framing and sheathing interior walls
- Proceed with underground utility work outside building footprint

BUDGET

Change Order Status (Based on Change Orders Approved to Date)

Contractor	Bid Award Amt	App Change Orders as of 11/12/21	Current CO %	Current Revised Contracts as of 11/12/21
E.R. Stuebner	\$15,701,000.00	\$111,607.90	0.71%	\$15,812,607.90
Cedar Electric, Inc.	\$3,461,000.00	--	0.00%	\$3,461,000.00
Trefz Mechanical, Inc. (PC)	\$1,524,067.00	--	0.00%	\$1,524,067.00
Trefz Mechanical, Inc. (MC)	\$3,467,844.00	--	0.00%	\$3,467,844.00
Total Contract Amounts	\$24,153,911.00	\$111,607.90	0.46%	\$24,265,518.90

BUDGET

Pending Change Orders

Contractor	Contractor PCO #	Description of Work	PCO Amount	Status
		None at this time		



**EAGLEVILLE ELEMENTARY SCHOOL
ADDITION AND RENOVATIONS PROJECT
NOVEMBER 2021 BOARD REPORT**



New Addition Brick

- Completed face brick at new addition
- Continuing topsoiling and hydroseeding around site
- Preparing for concrete sidewalks at new front entrance



Phase 3 Windows & Cast Stone

- Completed aluminum windows throughout addition
- Completed cast stone throughout addition
- Installing glass throughout addition



Interior Addition

- Installing APC grid in remaining corridor
- Installing carrier system for linear metal ceilings
- Performing painting throughout all Phase 3 areas





**EAGLEVILLE ELEMENTARY SCHOOL
ADDITION AND RENOVATIONS PROJECT
NOVEMBER 2021 BOARD REPORT**



Interior Addition / Phase 3

- Completed APC grid at new Flex Room
- Installing ceramic tiling throughout Phase 3 areas
- Began installing linear metal ceilings

Upcoming Work – November – 2021

- Complete OH fixtures and finishes throughout Phase 3 areas.
- Complete linear metal and APC ceilings throughout Phase 3 areas.
- Complete ceramic tiling throughout Phase 3.
- Complete all aluminum and glazing
- Begin APC tile installations throughout Phase 3 areas.
- Begin VCT and Terrazzo tile flooring at Phase 3 areas.
- Begin installation of PLAM case work
