


## Fiber Line Relocation

- Located existing line and spliced to relocated line.
- Installed exterior conduit at building to run above ceiling.
- Tied-in new fiber to School's indoor-fiber network.

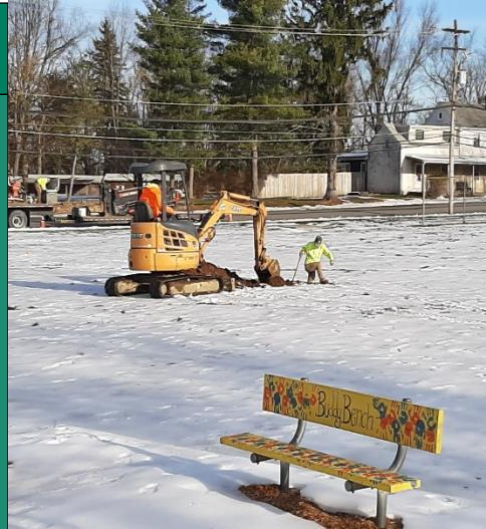

## Playground Equipment Relocation

- Playground equipment removed from behind building.
- Equipment re-installed at location near front bus loop.
- New mulch delivered for play surface.



## Tree Removal/Site Clearing

- Began clearing trees within the construction site footprint.
- Cleaning up fallen trees in tree row around the site.
- Debris moved offsite.





**ARROWHEAD ELEMENTARY SCHOOL PROJECT  
JANUARY 2021 BOARD REPORT**



**Upcoming Work – January - February 2021**

- Installation of construction fencing (Starting: 1/21/21)
- Demolition of modulares connected to existing building (Starting: 1/25/21)
- Removal of electrical feed to modulares and relocate other utilities passing through new construction footprint
- Install E&S controls and begin site work (strip topsoil, begin basin construction, etc.)
- Setup construction trailers and prep lay-down area
- Prep new building pad

**BUDGET**

**Change Order Status (Based on Change Orders Approved to Date)**

Contractor	Bid Award Amt\$	App Change Orders as of 1/22/21	Current CO %	Current Revised Contracts as of 1/22/21
E.R. Steubner	\$15,701,000.00	--	0%	\$15,701,000.00
Cedar Electric, Inc.	\$3,461,000.00	--	0%	\$3,461,000.00
Trefz Mechanical, Inc. (PC)	\$1,524,067.00	--	0%	\$1,524,067.00
Trefz Mechanical, Inc. (MC)	\$3,467,844.00	--	0%	\$3,467,844.00
<b>Total Contract Amounts</b>	\$24,153,911.00	\$0.00	0%	\$24,153,911.00

**BUDGET**

**Pending Change Orders**

Contractor	Contractor PCO #	Description of Work	PCO Amount	Status
		None at this time		

**Board Action Items**

1. Geotech Proposal Review and Approval – Soil and Concrete Testing. Hillis-Carnes Proposal in the amount of \$34,638.00.
