


Topsoil Removal/Structural Fill

- Removing topsoil to expose subgrade
- Stockpiled topsoil onsite for use in later phases
- Installed structural fill and compacted for building pad

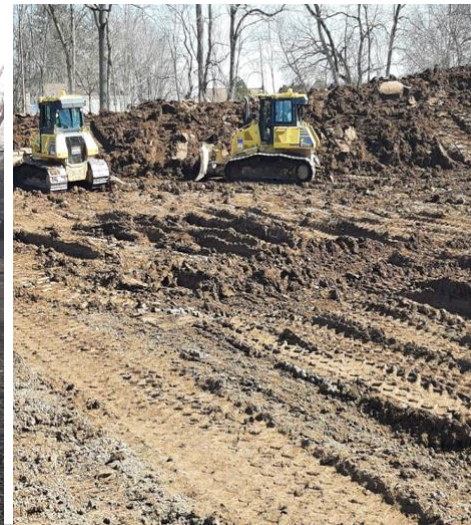

Utility Install and Connections

- Installed full length of exterior sanitary piping and manholes to service new building
- Relocated waterline to existing building
- Installed new waterline service

Temporary Electric Service

- Connected to main electric service in existing building
- Installed cable on roof of existing building
- Connected temp transformer
- Fed cable underground to office trailer location





**ARROWHEAD ELEMENTARY SCHOOL PROJECT
MARCH 2021 BOARD REPORT**



Upcoming Work – March – April 2021

- Completion of soils mitigation as laid out in GC-PCO #1
- Completion of building pad fill to finished elevation
- Installation of permanent electrical/communication duct bank servicing the new building
- Begin excavating for and construction of building footers once pad work is complete
- Begin underground/underslab utilities within the building footprint
- Remaining office trailers and sea-can storage delivered to the site

BUDGET

Change Order Status (Based on Change Orders Approved to Date)

Contractor	Bid Award Amt	App Change Orders as of 3/12/21	Current CO %	Current Revised Contracts as of 3/12/21
E.R. Stuebner	\$15,701,000.00	--	0%	\$15,701,000.00
Cedar Electric, Inc.	\$3,461,000.00	--	0%	\$3,461,000.00
Trefz Mechanical, Inc. (PC)	\$1,524,067.00	--	0%	\$1,524,067.00
Trefz Mechanical, Inc. (MC)	\$3,467,844.00	--	0%	\$3,467,844.00
Total Contract Amounts	\$24,153,911.00	\$0.00	0%	\$24,153,911.00

BUDGET

Pending Change Orders

Contractor	Contractor PCO #	Description of Work	PCO Amount	Status
ER Stuebner	1 – Option #1	Remediation of unsuitable subgrade material within the building pad (Soil Cement Option)	\$75,700.00	Proposed

Board Action Items

- None at this time.
